BRHAT BANGALORE MAHANAGARA PALIKE
INSPECTION REPORT

Sl No	Decription	Details	Remarks
1	Name of Work	Improvements to Roadand drains at Tuba Layout in Ward No. 06 Thanisandra Village Limit	
2	Estimate Cost	20.00 Lakhs	
3	Administrative Approved No and Date	554/13-14, Date. 23.12.2013	
4	Technical sanction No. and Date	273/13-14, Date. 01.02.2014	
5	Job Code No. and P Code No.	006-14-000061	
6	Tender Direct Entrested to KRIDL	KRIDL	
7	if Tender, Tender Notification No. Date and Publication in daily news Paper	Not Applicable	
8	Tender Approved Details	Not Applicable	
9	Work Order No and Date	417/2013-14, Date. 21.02.2014	
10	Stipulation time of Completion	90 Days	
11	Actiual Date of Commencement	02.07.2014	
12	Actiual Date of Completion	27.07.2014	
13	Delay if any	Nil	

	Reson for Delay	Nil	
15	Payment made till date.	Nil	
16	Status of Work	Completed	
17	Photograph verfied	Enclosed	
18	Date of Inspection	16.07.2015	
19	MB No. and Page No.	Mb 2561 Page No.256015-22	
20	BR No. and Date	256/31.07.2014	
21	Test Result	Quality Test Report submitted by Bangalore University Dept of Civil Engineering is verified and Enclosed	
22	Section officer	Sri K Devegowda J.E	
23	Sub Division Office	Sri Shivakumar Goudar AEE Byatarayanaprua Sub Division	
24	Observation		
a	Work Quality	Satisfactory	
b	Comments	Work completed as per MB	

16/7/15

Y C Kale gowda
Executive Engineer (Retd)

Executive Engineer
Byatarayanapura Division
Yelahanka Zone, B.B.M.P.
Bangalore - 560 092

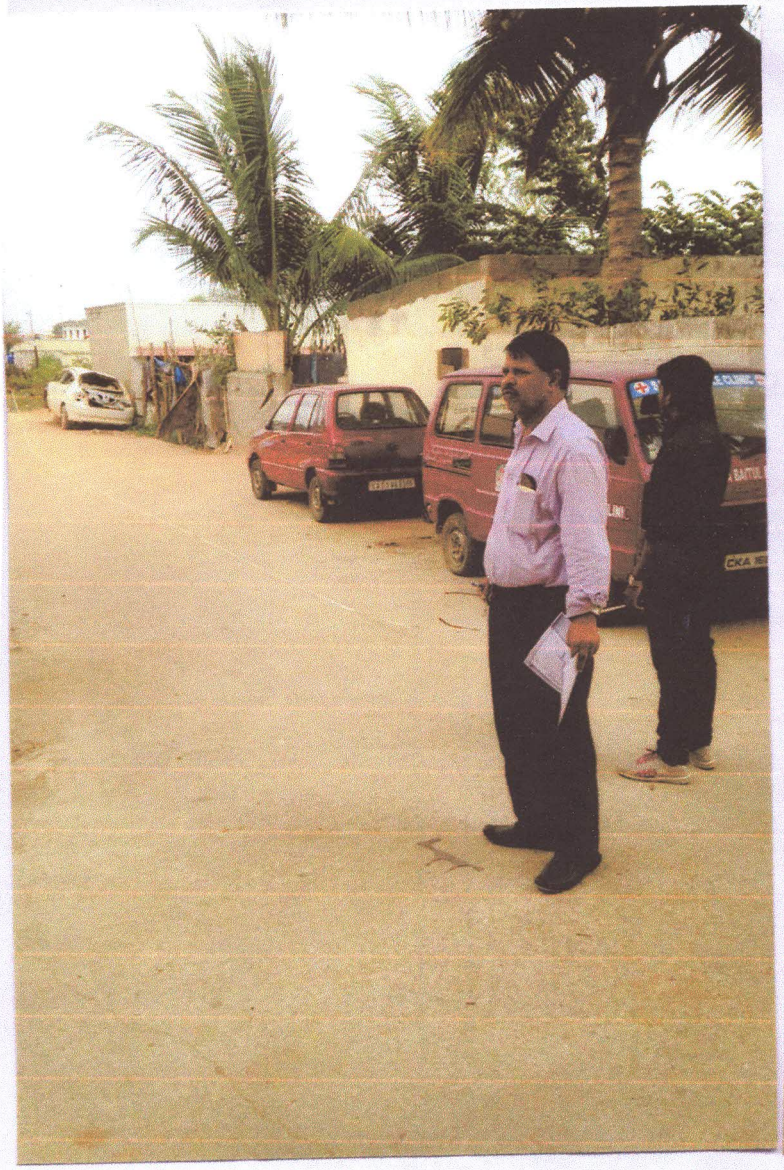

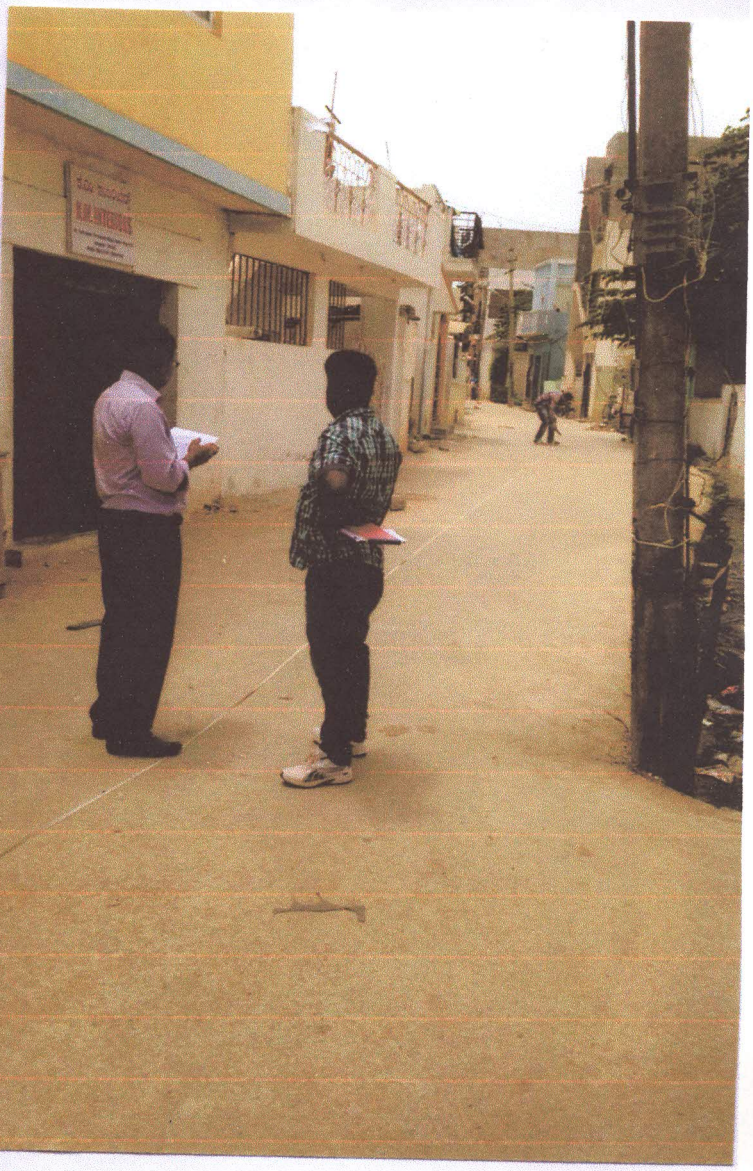

ಸಹಾಯಕ ಅಭಿಯಂತರರು
ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ
